




# CENTRAL FLORIDA EXPRESSWAY AUTHORITY


## WEKIVA PARKWAY CONSTRUCTION UPDATE

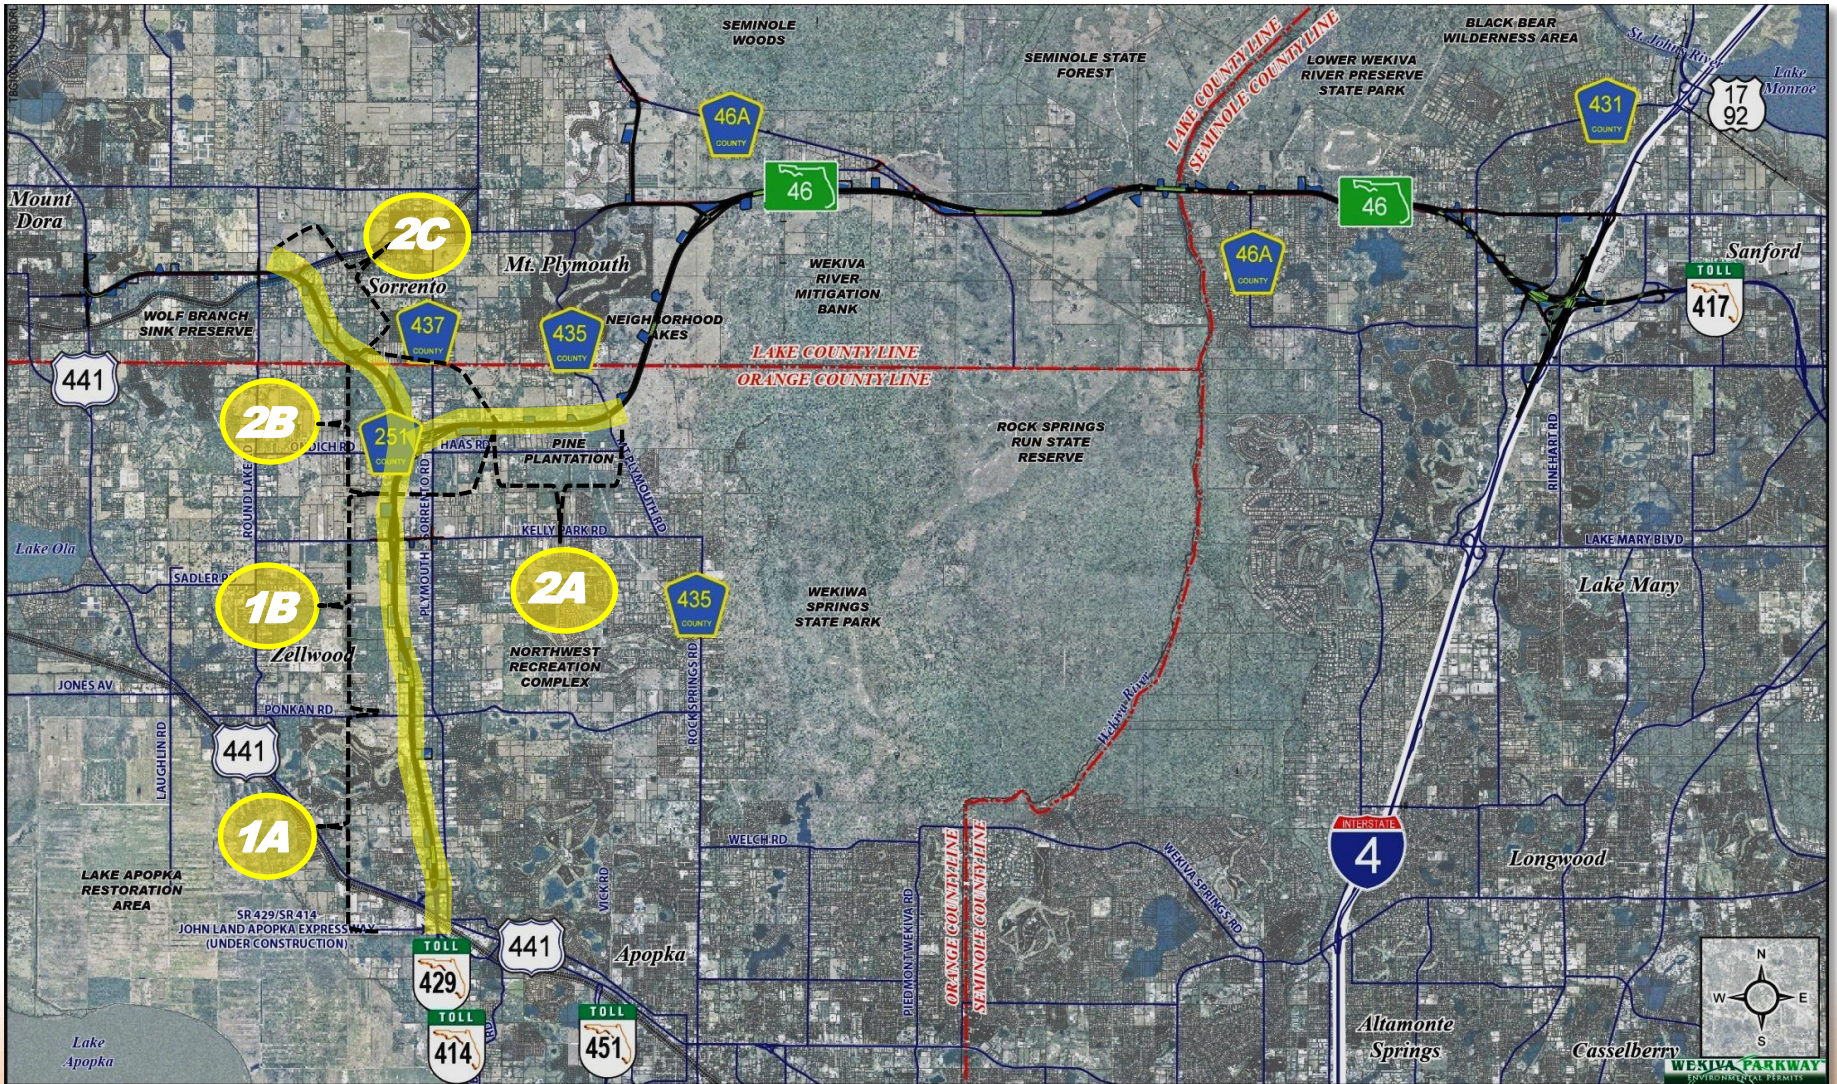

# WEKIVA PARKWAY

## 5 projects under construction

- 10 miles
- ~465 construction workers on the project on any given day
- \$271.6 million under contract
- \$119.6 million earned thru 10/25/16
- 44% complete

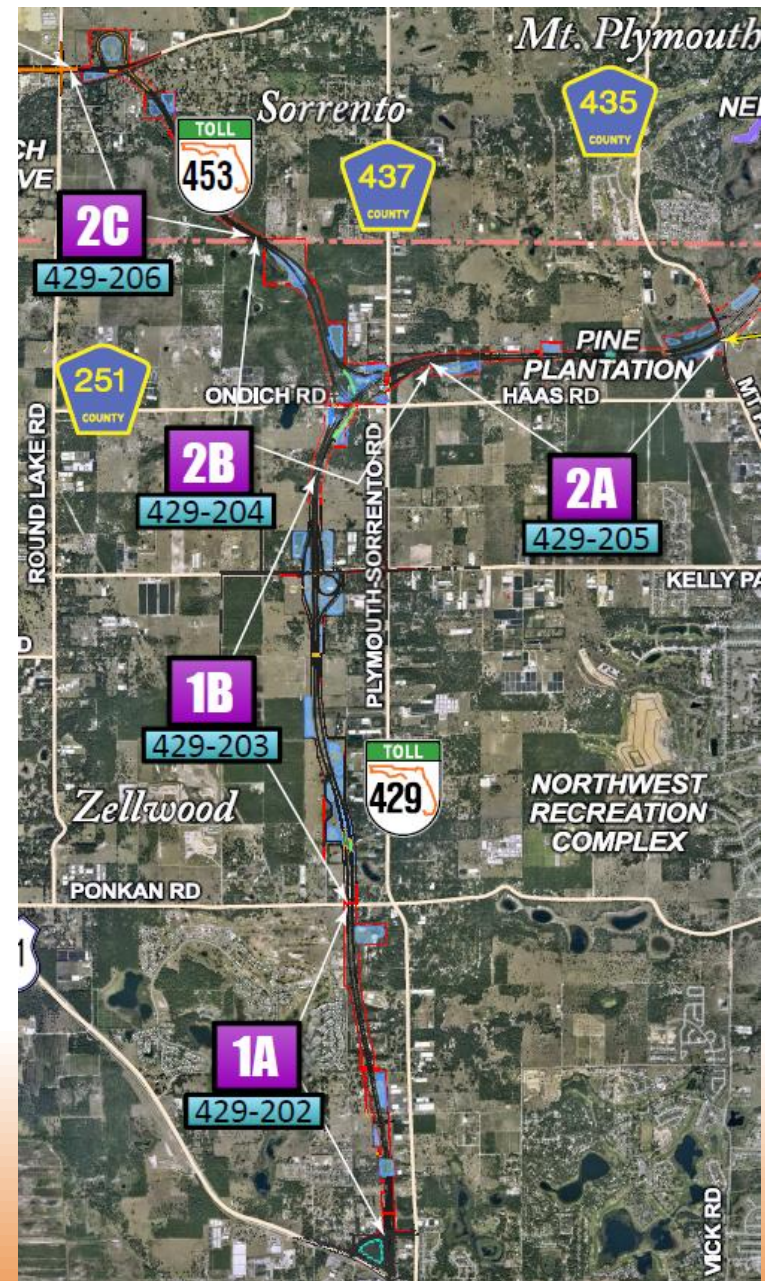



# Section 429-202 (1A)

*From North of US 441 to North of Ponkan Rd.*

Started: June 8, 2015

Contractor:  
Prince Construction

Contract: \$56.3 million

Earned: \$38.3 million

Time: 679 calendar days

Percent Complete: 68%






CENTRAL FLORIDA EXPRESSWAY AUTHORITY



CENTRAL FLORIDA EXPRESSWAY AUTHORITY



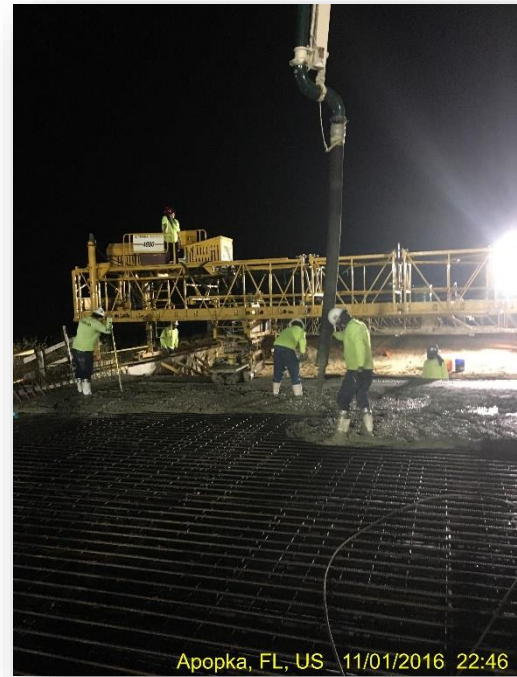





CENTRAL FLORIDA EXPRESSWAY AUTHORITY



# Section 429-203 (1B)

From North of Ponkan Rd. to North of a New Kelly Park Road Interchange

Started: August 3, 2015

Contractor:  
Superior Construction

Contract: \$46.5 million

Earned: \$35.8 million

Time: 600 calendar days

Percent Complete: 77%





CENTRAL FLORIDA EXPRESSWAY AUTHORITY




11/3/2016 2:50 PM



CENTRAL FLORIDA EXPRESSWAY AUTHORITY



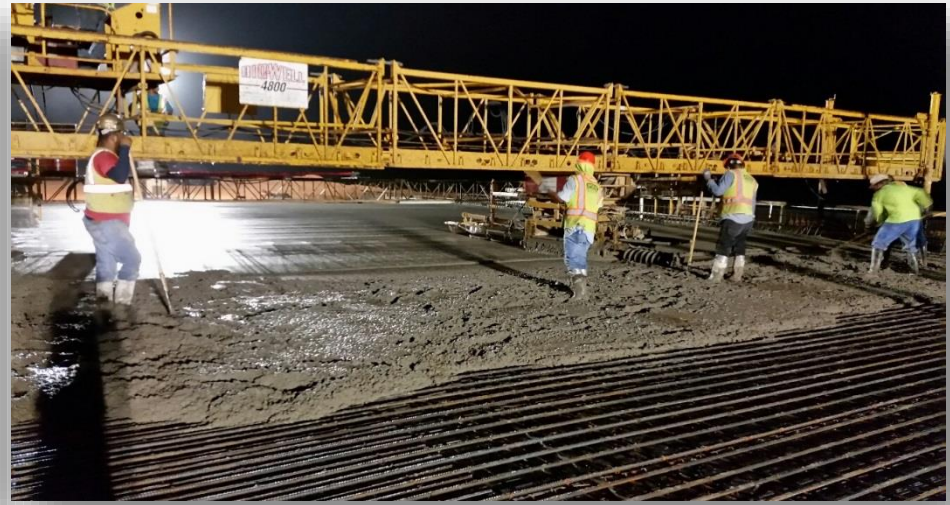



# Section 429-204 (2B)

*Systems Interchange extending Wekiva Parkway (SR 429) northeast toward Sanford and SR 453 toward Mount Dora*

Started: January 4, 2016

Contractor:


Southland Construction

Contract: \$80.7 million

Earned: \$28 million

Time: 730 calendar days

Percent Complete: 35%

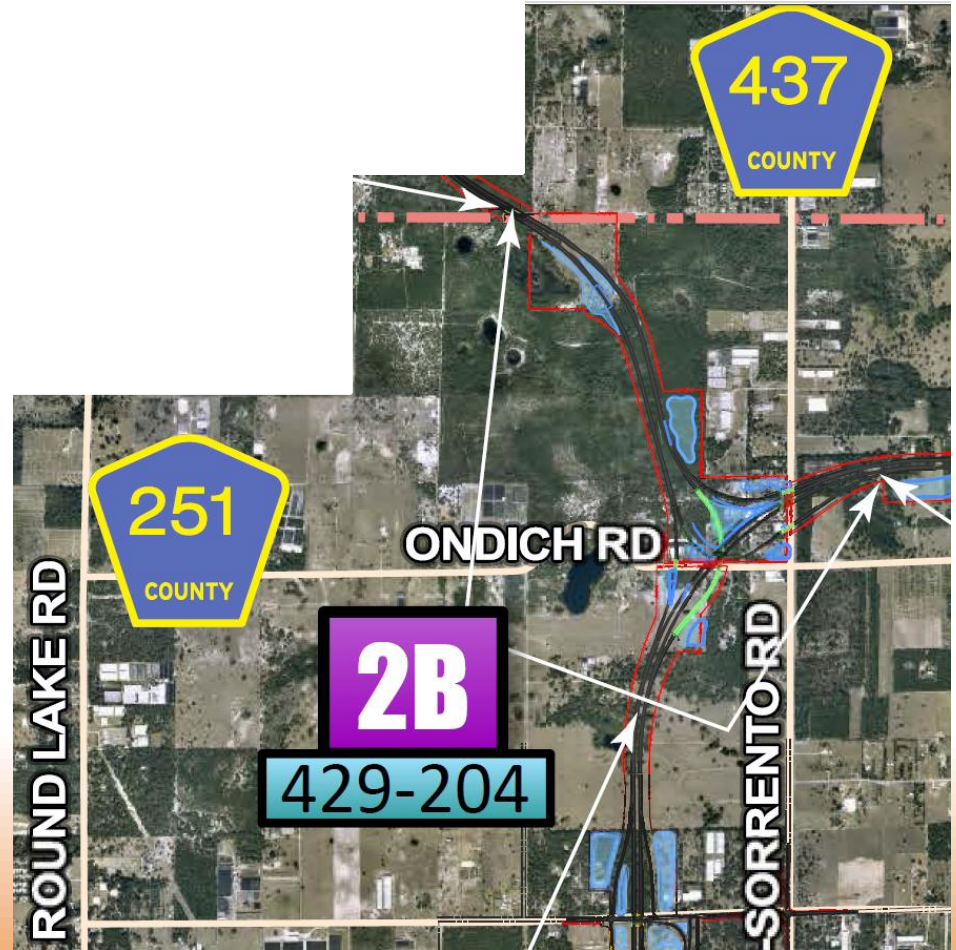



CENTRAL FLORIDA EXPRESSWAY AUTHORITY





CENTRAL FLORIDA EXPRESSWAY AUTHORITY







# Section 429-205 (2A)

*Wekiva Parkway (SR 429) from the Systems Interchange east to FDOT's completed Section 4A at CR 435*

Started: August 1, 2016

Contractor:

Superior Construction


Contract: \$38.6 million

Earned: \$4.4 million

Time: 570 calendar days

Percent Complete: 11%



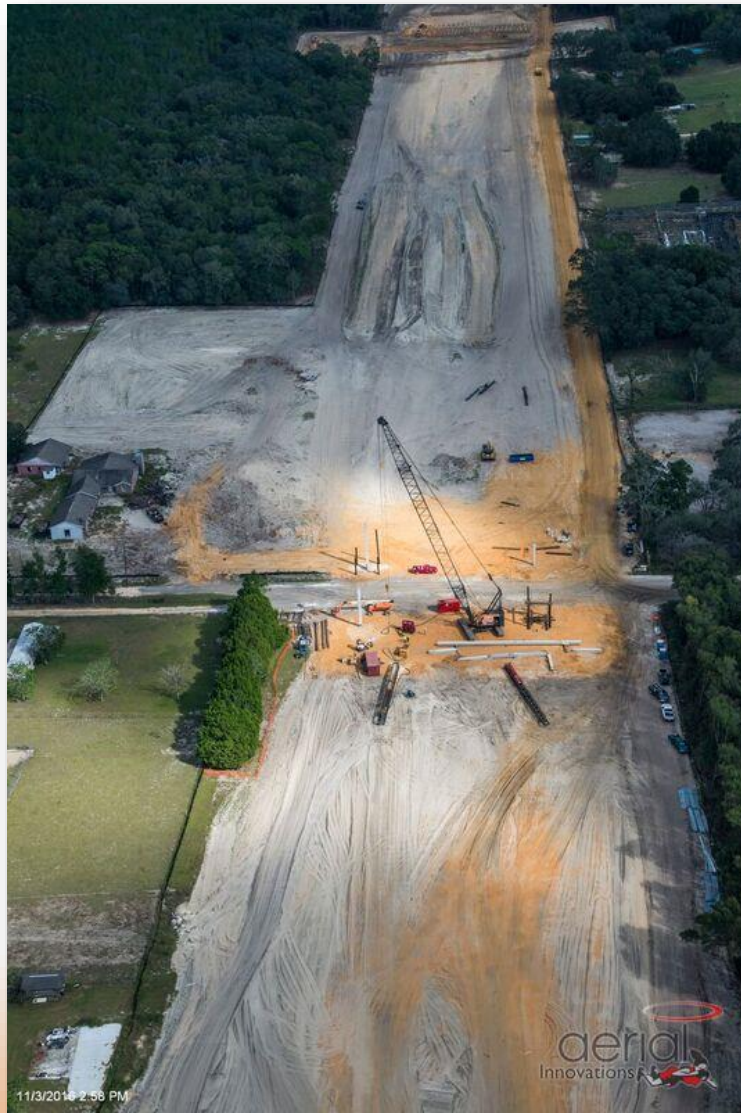





## Section 429-206 (2C)

*North-West leg of the Wekiva Parkway (SR 453) extending from the Lake County Line to SR 46 toward Mount Dora*

Started: May 2, 2016

Contractor: GLF Construction

Contract: \$49.5 million

Earned: \$13 million

Time: 600 calendar days

Percent Complete: 26%









# When Complete, we will have:

- Excavated ~3.6 million Cubic Yards of Earth (18 Large Cruise Ships)
- Built ~8.4 million Cubic Yards of Embankment (42 Large Cruise Ships)
- Built ~58 Lane Miles of New Expressway
- Driven ~ 40 Miles of Foundation Piles
- Built 40 New Bridges
- Planted ~ 440,000 Square Yards of Seed & Mulch (83 Football Fields)
- Placed ~ 2.3 million Square Yards of Sod (428 Football Fields)



## WEKIVA PARKWAY CCEI & COMPLIANCE TEAMS

- **429-202:** **RK&K**, CDM Smith, RS&H, PICS (DBE), PSI, URS, Terracon, Elipsis (DBE) AMEC, Mehta (DBE)
- **429-203:** **GAI**, DRMP, PI Consulting (DBE), Page One, Ardaman, FGE, GPI, Mehta (DBE)
- **429-204:** **A2** (DBE), Figg, RK&K, DRMP, GCI (DBE), Mehta (DBE), Gannett Fleming & Page One (DBE)
- **429-205:** **KCCS**, Elipsis (DBE), GRL, PICS (DBE), Page One (DBE) & Echezabal (DBE)
- **429-206:** **Jacobs**, Metric, FGE, Aerial Innovations, Ardaman, Elipsis (DBE) & Mehta (DBE)
- **Corridor Consultant:** **CH2M**
- **Corridor-Wide Compliance:** **MTN Resources**



# WEKIVA PARKWAY OPENING PLAN

- Mid 2017: Open Wekiva Parkway from Connector Road to Kelly Park Road [Sections 1A (429-202) & 1B (429-203)]
- Early 2018: Open remainder of CFX Wekiva Projects [Sections 2A, 2B & 2C (429-204, 429-205 & 429-206)]
